

Weekly News Letter September 16, 2016



A Week In Review

- Site Work:
 - Continue to lower ground water behind buildings 23 and 25 to continue installing underground water line
 - Storm water line is installed in courtyard
- Building 23W:
 - Continued installing metal stud framing
 - Continued overhead electrical rough-in
 - Continued putting up sheet rock in building 23
 - Finished installing hollow metal door and window frames
- Building 25W:
 - Completed installing metal framing around exterior walls and above CMU at women's gang restroom
 - Continued installing mechanical and electrical overhead rough-in
 - Completed framing East and South exterior walls
 - Installed exterior wall sheathing
 - Poured back slab for northwest area for mechanical room and miscellaneous areas
- Building infill connecting 23W & 25W
 - Completed framing
- Day Center Demolition:
 - Nearly completed interior demolition of West half of Day Center


What's Next?

- Site Work:
 - Continuing to keep the water table low during utility installation
 - Continuing utility installation
 - Installing sanitary sewer line in courtyard
- Building:
 - Exterior panel and roof repairs will begin
 - Exterior framing & hat channel
 - Mechanical and electrical rough in 23W and 25W
 - Spray foam insulation to begin

Community Impacts

- Work Hours: 6AM - 4:30 PM
- SRM daily operations have moved to 19 and 21 W Las Vegas to allow for the demolition and remodel of the shelter
- Site access is limited throughout:
 - A construction fence has been placed up in the courtyard to safely isolate construction activities
- Nunn Construction has hired four members of the SRM program!!! The three newest hires are members of a security team that will help keep the project site secure throughout the remaining duration

Construction Site Overview

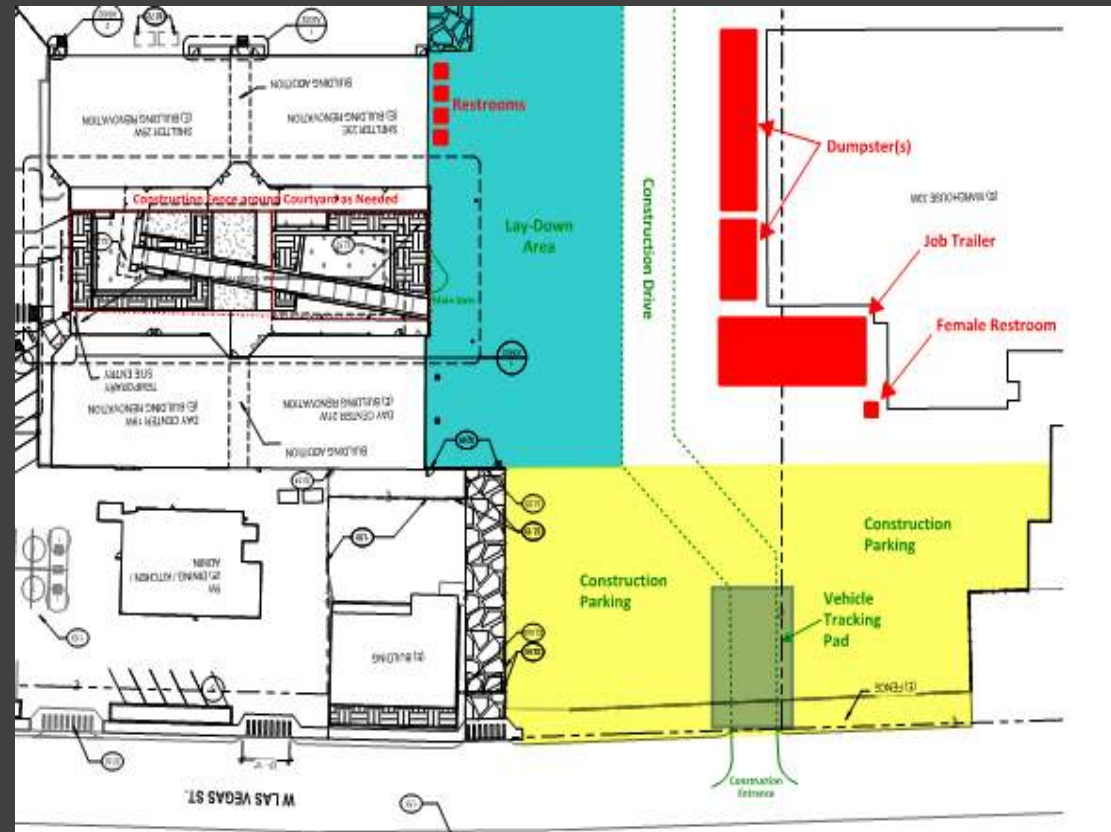

Subcontractors On Site

- *Gen Contractor: Nunn Construction*
- Dewatering: Rain for Rent
- Utilities: A&R, CSU
- Dirt work: Lambert & Sons
- Plumbing: Olson Plumbing
- Electrical: Greiner Electric
- Mechanical: Colorado Sheet Metal
- Metal Framing: Tri City Drywall
- Concrete: Peak Concrete
- Drilling: Ludwig Drilling
- Surveyor: Polaris

Daily Weather History & Observations

| 2016 | Temp. (°F) | | | Dew Point (°F) | | | Humidity (%) | | | Sea Level Press. (in) | | | Visibility (mi) | | | Wind (mph) | | | Precip. (in) | Events |
|------|------------|-----|-----|----------------|-----|-----|--------------|-----|-----|-----------------------|-------|-------|-----------------|-----|-----|------------|-----|------|--------------|---------------------|
| Sep | high | avg | low | high | avg | low | high | avg | low | high | avg | low | high | avg | low | high | avg | high | sum | |
| 11 | 88 | 70 | 52 | 39 | 28 | 17 | 63 | 37 | 10 | 30.06 | 29.90 | 29.74 | 10 | 10 | 10 | 22 | 6 | 25 | 0.00 | |
| 12 | 82 | 69 | 56 | 49 | 37 | 26 | 77 | 46 | 14 | 30.12 | 29.86 | 29.72 | 10 | 10 | 6 | 29 | 11 | 37 | 0.04 | Rain , Thunderstorm |
| 13 | 65 | 57 | 49 | 47 | 46 | 44 | 93 | 73 | 52 | 30.35 | 30.16 | 29.99 | 10 | 9 | 7 | 20 | 9 | 24 | 0.00 | |
| 14 | 75 | 63 | 50 | 49 | 47 | 35 | 93 | 63 | 33 | 30.30 | 30.14 | 29.92 | 10 | 6 | 0 | 24 | 12 | 29 | T | Fog |
| 15 | 82 | 67 | 51 | 43 | 35 | 22 | 64 | 38 | 11 | 30.08 | 29.93 | 29.80 | 10 | 10 | 10 | 36 | 11 | 43 | 0.00 | |
| 16 | 70 | 58 | 45 | 37 | 35 | 31 | 68 | 44 | 24 | 30.13 | 30.04 | 29.97 | 10 | 10 | 10 | 17 | 9 | 26 | 0.00 | |




Installed
exterior
sheathing on
building 23
and 25



Fluid applied vapor
barrier applied to
existing stucco
building 25



Offices and staff
restrooms
framed out

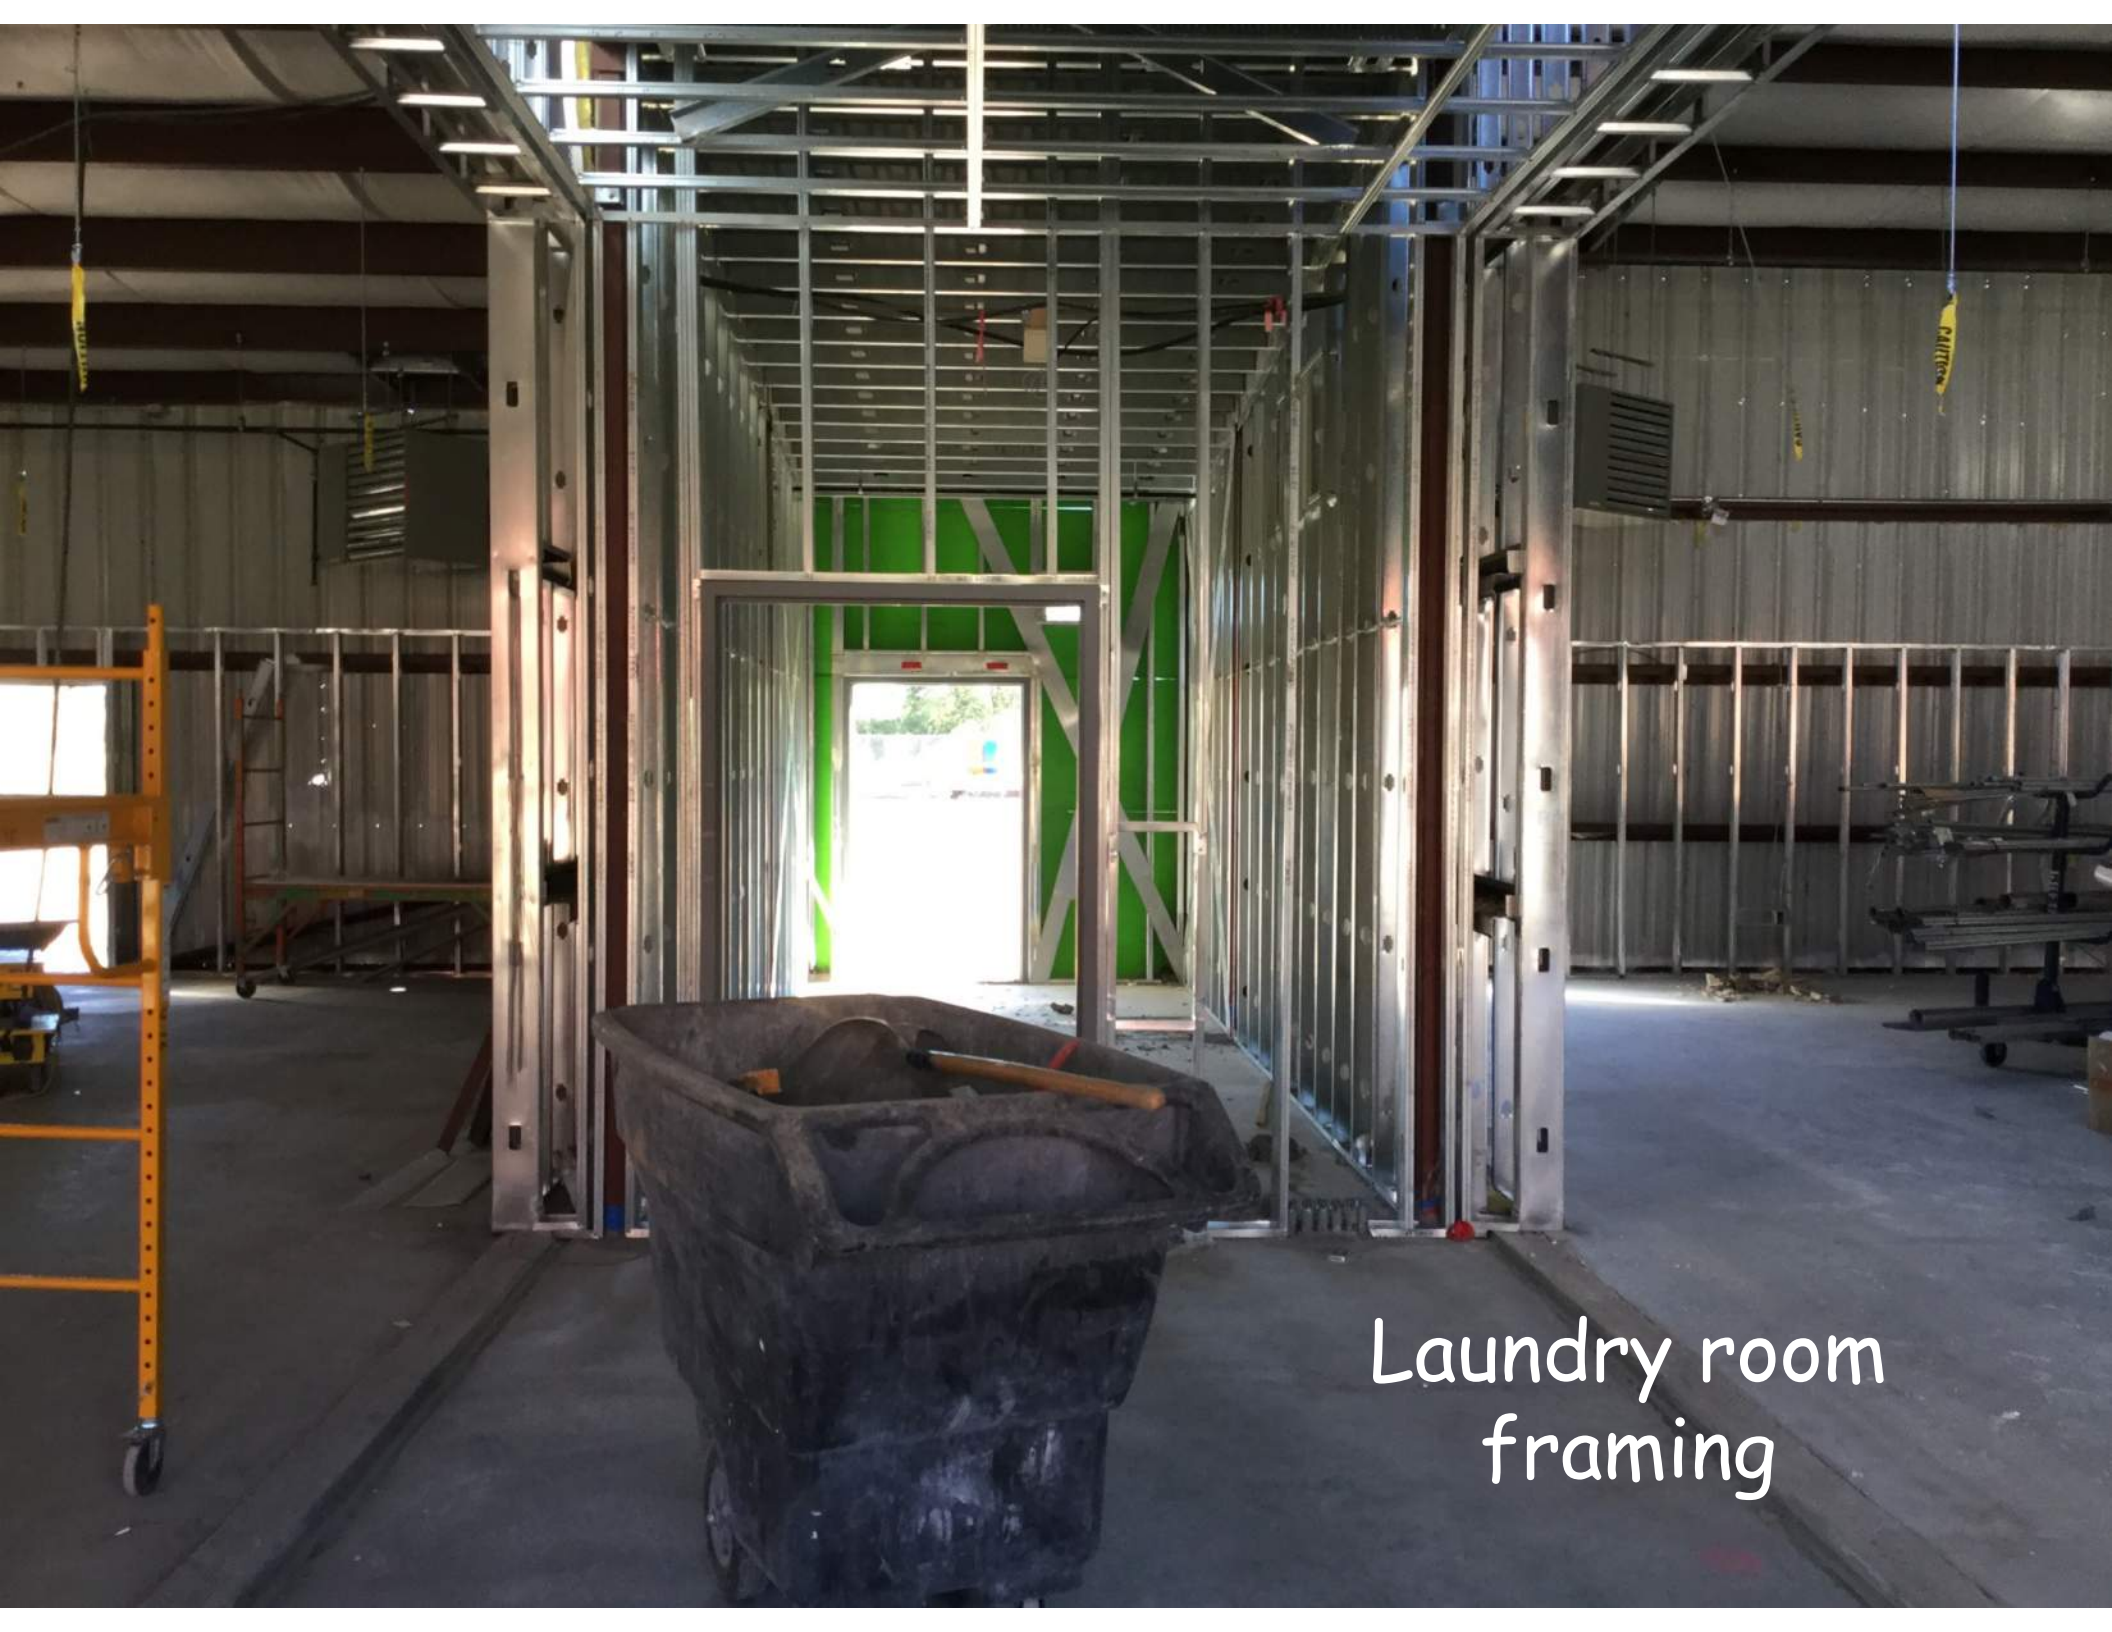

Laundry room
framing
