

## Weekly News Letter October 7, 2016



# A Week In Review


- Site Work:
  - Completed storm drain on west side of building 23
  - Finished installing Structural Steel for canopies in the courtyard
  - Started forming footers for planter in the courtyard
  - Painted steel columns in courtyard
- Building 23W:
  - Completed installing metal stud framing
  - Continued putting up sheet rock and started taping and bedding
  - Started installing fire sprinkler mains and branch lines
  - Started painting Hardie board panels
  - Continued storefronts and glazing
  - Started installing roof insulation
  - Installed resinous flooring in gang restroom
- Building 25W:
  - Continued installing metal stud framing
  - Continued installing mechanical and electrical overhead rough-in
  - Installed resinous flooring in gang restroom
  - Continued storefronts and glazing
- Building infill connecting 23W & 25W
  - Started roof

# What's Next?

- Site Work:
  - Completing all underground utilities in the courtyard
  - Completing existing water line repairs on South side of site
  - Pouring concrete for planter walls in courtyard
  - Start courtyard walls and seating
- Building:
  - Exterior roof repairs will begin
  - Begin sheetrock installation after in-wall inspections are complete
  - Begin painting of interior walls
  - Hard surface flooring installation
  - Light fixtures

- Work Hours: 6AM - 4:30 PM
- SRM daily operations have moved to 19 and 21 W Las Vegas to allow for the demolition and remodel of the shelter
- Site access is limited throughout:
  - A construction fence has been placed up in the courtyard to safely isolate construction activities
- Nunn Construction has hired four members of the SRM program!!! The three newest hires are members of a security team that will help keep the project site secure throughout the remaining duration

Construction Site Overview

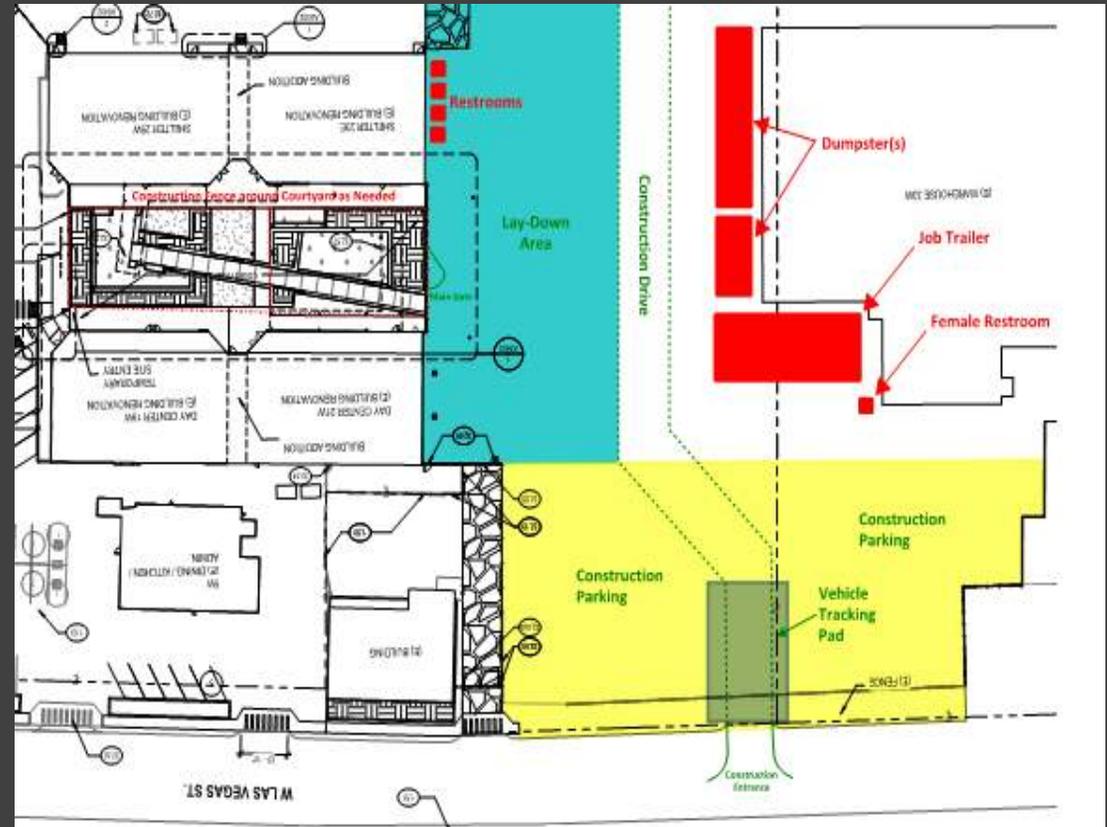

# Subcontractors On Site

- *Gen Contractor:* Nunn Construction
- *Dewatering:* Rain for Rent
- *Utilities:* A&R, CSU
- *Dirt work:* Lambert & Sons
- *Plumbing:* Olson Plumbing
- *Electrical:* Greiner Electric
- *Mechanical:* Colorado Sheet Metal
- *Metal Framing:* Tri City Drywall
- *Concrete:* Peak Concrete
- *Roofing:* Central States
- *Glass:* Ryan Glass
- *Steel:* Kutch Steel
- *Insulation:* MATO Insulation

# Weekly Weather

## Daily Weather History & Observations

2016	Temp. (°F)			Dew Point (°F)			Humidity (%)			Sea Level Press. (in)			Visibility (mi)			Wind (mph)			Precip. (in)
	high	avg	low	high	avg	low	high	avg	low	high	avg	low	high	avg	low	high	avg	high	sum
2	81	65	48	45	41	36	80	51	21	30.02	29.91	29.74	10	10	10	23	8	27	0.00
3	78	65	52	43	30	15	71	42	12	29.72	29.51	29.37	10	10	10	39	20	53	T
4	67	55	42	23	14	7	45	29	12	29.86	29.66	29.50	10	10	10	21	8	27	0.00
5	68	52	35	24	18	12	48	30	11	29.96	29.86	29.77	10	10	10	26	10	32	0.00
6	60	47	33	37	30	20	76	53	29	30.29	30.02	29.81	10	10	10	30	12	36	T
7	36	33	30	30	28	26	82	80	79	30.39	30.34	30.27	10	10	10	8	6	-	0.00



Painting Hardie Board outside building 23



Storefronts & glazing installed in buildings 23 & 25



Started installing  
the epoxy floor in  
the men's gang  
restroom



Fire sprinkler  
pipes being hung  
in building 23



Setting forms for  
concrete planter in  
courtyard
